

**Muhammad Fahad    BSCS23047**  
**Humayun Naseem    BSCS23002**  
**Abdul wahid Awan    BSCS23189**

## **Project 1: Custom Software Development Project**

### **Proposed processes:**

#### **Phase 1: Project Initiation (1-2 weeks)**

##### **Key Activities:**

- Stakeholder identification and engagement
- Requirements validation and documentation
- Team formation and role assignment
- Project charter creation
- Risk assessment and mitigation planning

##### **Deliverables:**

- Project Charter
- Stakeholder Register
- Requirements Document
- Risk Register
- Team Structure Document

##### **Decision Gate:**

Gate 1: Project approval and resource allocation confirmation

#### **Phase 2: Planning & Design (2-3 weeks)**

##### **Key Activities:**

- Sprint planning and backlog creation
- Technical architecture design
- User story mapping

- Quality assurance planning
- Communication plan establishment

**Deliverables:**

- Product Backlog
- Sprint Plan
- Technical Architecture Document
- User Stories and Acceptance Criteria
- Quality Assurance Plan

**Decision Gate:**

Gate 2: Design approval and development readiness

**Phase 3: Development & Testing (12-16 weeks)**

**Key Activities:**

- Iterative development in 2-week sprints
- Continuous integration and testing
- Regular stakeholder demos
- Risk monitoring and issue resolution
- Change control management

**Deliverables:**

- Working Software Increments
- Test Reports
- Sprint Reviews
- Updated Risk Register
- Change Requests (if any)

**Decision Gates:**

Gate 3a-3f: End of each sprint - Continue/Adjust/Stop decisions

**Phase 4: Deployment & Closure (1-2 weeks)**

**Key Activities:**

- User acceptance testing
- Production deployment
- User training and documentation
- Project closure activities
- Lessons learned documentation

#### **Deliverables:**

- Deployed Software System
- User Documentation
- Project Closure Report
- Lessons Learned Document
- Support Transition Plan

#### **Decision Gate:**

Gate 4: Project completion and handover approval

### **Justification and references to standards:**

#### **PMBOK 7 References**

- Project Performance Domains: Stakeholder, Team, Development Approach, Planning, Project Work, Delivery, Measurement, Uncertainty
- Tailoring Considerations: Development approach (iterative), project complexity (moderate), team experience (experienced)
- Value Delivery: Incremental value delivery through working software


#### **PRINCE2 References**

- Themes: Business Case (lightweight), Organization (small team), Quality (continuous testing), Plans (sprint-based), Risk (iterative assessment), Change (agile change control), Progress (sprint reviews)
- Processes: Starting up (initiation), Directing (steering committee), Initiating (planning), Managing Product Delivery (sprints), Controlling Stages (sprint management), Closing (project closure)
- Tailoring: Simplified documentation, reduced formality, frequent Checkpoints

## **ISO 21500 References**

- Project Management Processes: Initiating (stakeholder identification), Planning (scope and schedule), Executing (development), Monitoring (sprint tracking), Closing (handover)
- Knowledge Areas: Scope, Schedule, Cost, Quality, Risk, Resources, Stakeholder, Communication
- Adaptation: Scaled processes for project size and complexity

**Flow Diagram**

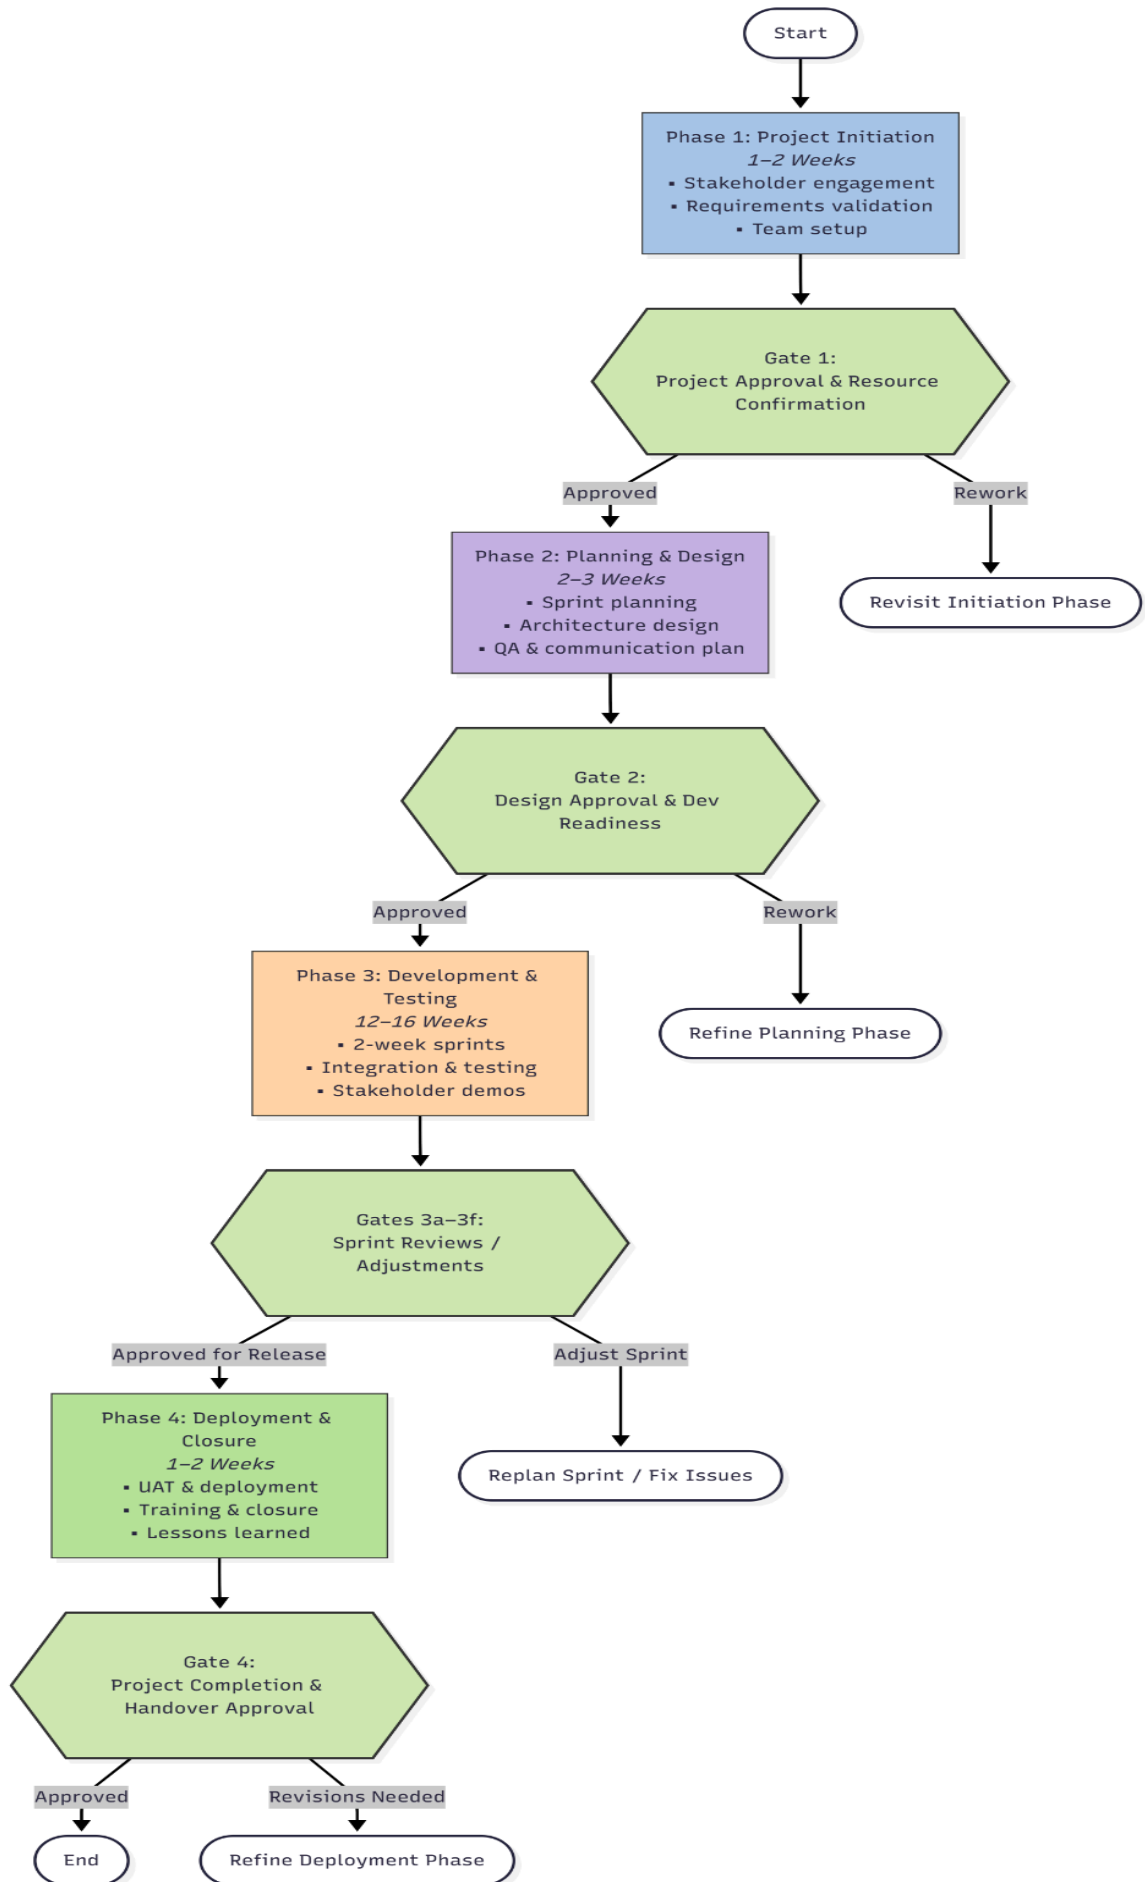

## **Project 2 : Enterprise System Implementation**

### **Proposed processes:**

#### **Phase 1: Pre-Project & Initiation (2-3 months)**

##### **Key Activities:**

- Business case development and approval
- Comprehensive stakeholder analysis
- Project charter and mandate creation
- Governance structure establishment
- Initial risk assessment and compliance review
- Vendor selection and contracting

##### **Deliverables:**

- Approved Business Case
- Project Charter and Mandate
- Governance Structure Document
- Stakeholder Register and Analysis
- Initial Risk Register
- Compliance Framework
- Vendor Contracts

##### **Decision Gate:**

Gate 1: Project authorization and funding approval

#### **Phase 2: Planning & Design (4-6 months)**

##### **Key Activities:**

- Detailed requirements gathering and analysis
- Enterprise architecture design
- Integration planning
- Data migration strategy
- Comprehensive project planning
- Quality management planning

- Training and change management planning

**Deliverables:**

- Detailed Requirements Specification
- Enterprise Architecture Design
- Integration Architecture
- Data Migration Plan
- Master Project Schedule
- Quality Management Plan
- Change Management Strategy
- Training Plan

**Decision Gate:**

Gate 2: Design approval and implementation authorization

**Phase 3: Implementation (8-12 months)****Key Activities:**

- System development/configuration
- Integration development and testing
- Data migration execution
- User acceptance testing
- Performance testing
- Security testing and compliance validation
- Change management activities
- Training delivery

**Deliverables:**

- Configured System Components
- Integration Solutions
- Migrated Data
- Test Reports and Evidence
- Compliance Certificates
- Trained Users



- Deployment Packages

**Decision Gates:**

Gates 3a-3d: Stage approvals for development, testing, training, and deployment readiness

**Phase 4: Deployment & Transition (2-4 months)****Key Activities:**

- Production deployment
- Go-live support
- Performance monitoring
- Issue resolution and stabilization
- Benefits realization monitoring
- Knowledge transfer
- Project closure activities

**Deliverables:**

- Live Production System
- Support Documentation
- Performance Reports
- Issue Resolution Reports
- Benefits Realization Report
- Project Closure Report
- Lessons Learned Document

**Decision Gate:**

Gate 4: Project completion and benefits realization confirmation

**Justification and references to standards:****PMBOK 7 References**

- Performance Domains: All domains with emphasis on Stakeholder (complex stakeholder landscape), Planning (comprehensive planning), Uncertainty (extensive risk management)

- Tailoring: Predictive approach with some adaptive elements, high formality level, extensive documentation
- Governance: Multi-tier governance structure with steering committee and project board


## **PRINCE2 References**

- Principles: Continued business justification, learn from experience, defined roles and responsibilities, manage by stages, manage by exception, focus on products, tailor to suit environment
- Themes: Full implementation of all seven themes with emphasis on Business Case, Organization, Quality, Plans, Risk, Change, Progress
- Processes: Complete process model with formal stage boundaries and decision points

## **ISO 21500 References**

- Process Groups: Comprehensive implementation of all five process groups with formal documentation
- Knowledge Areas: All ten knowledge areas with particular emphasis on Risk, Quality, Stakeholder, and Communication management
- Governance: Formal project governance aligned with organizational governance structures

**Workflow Diagram**

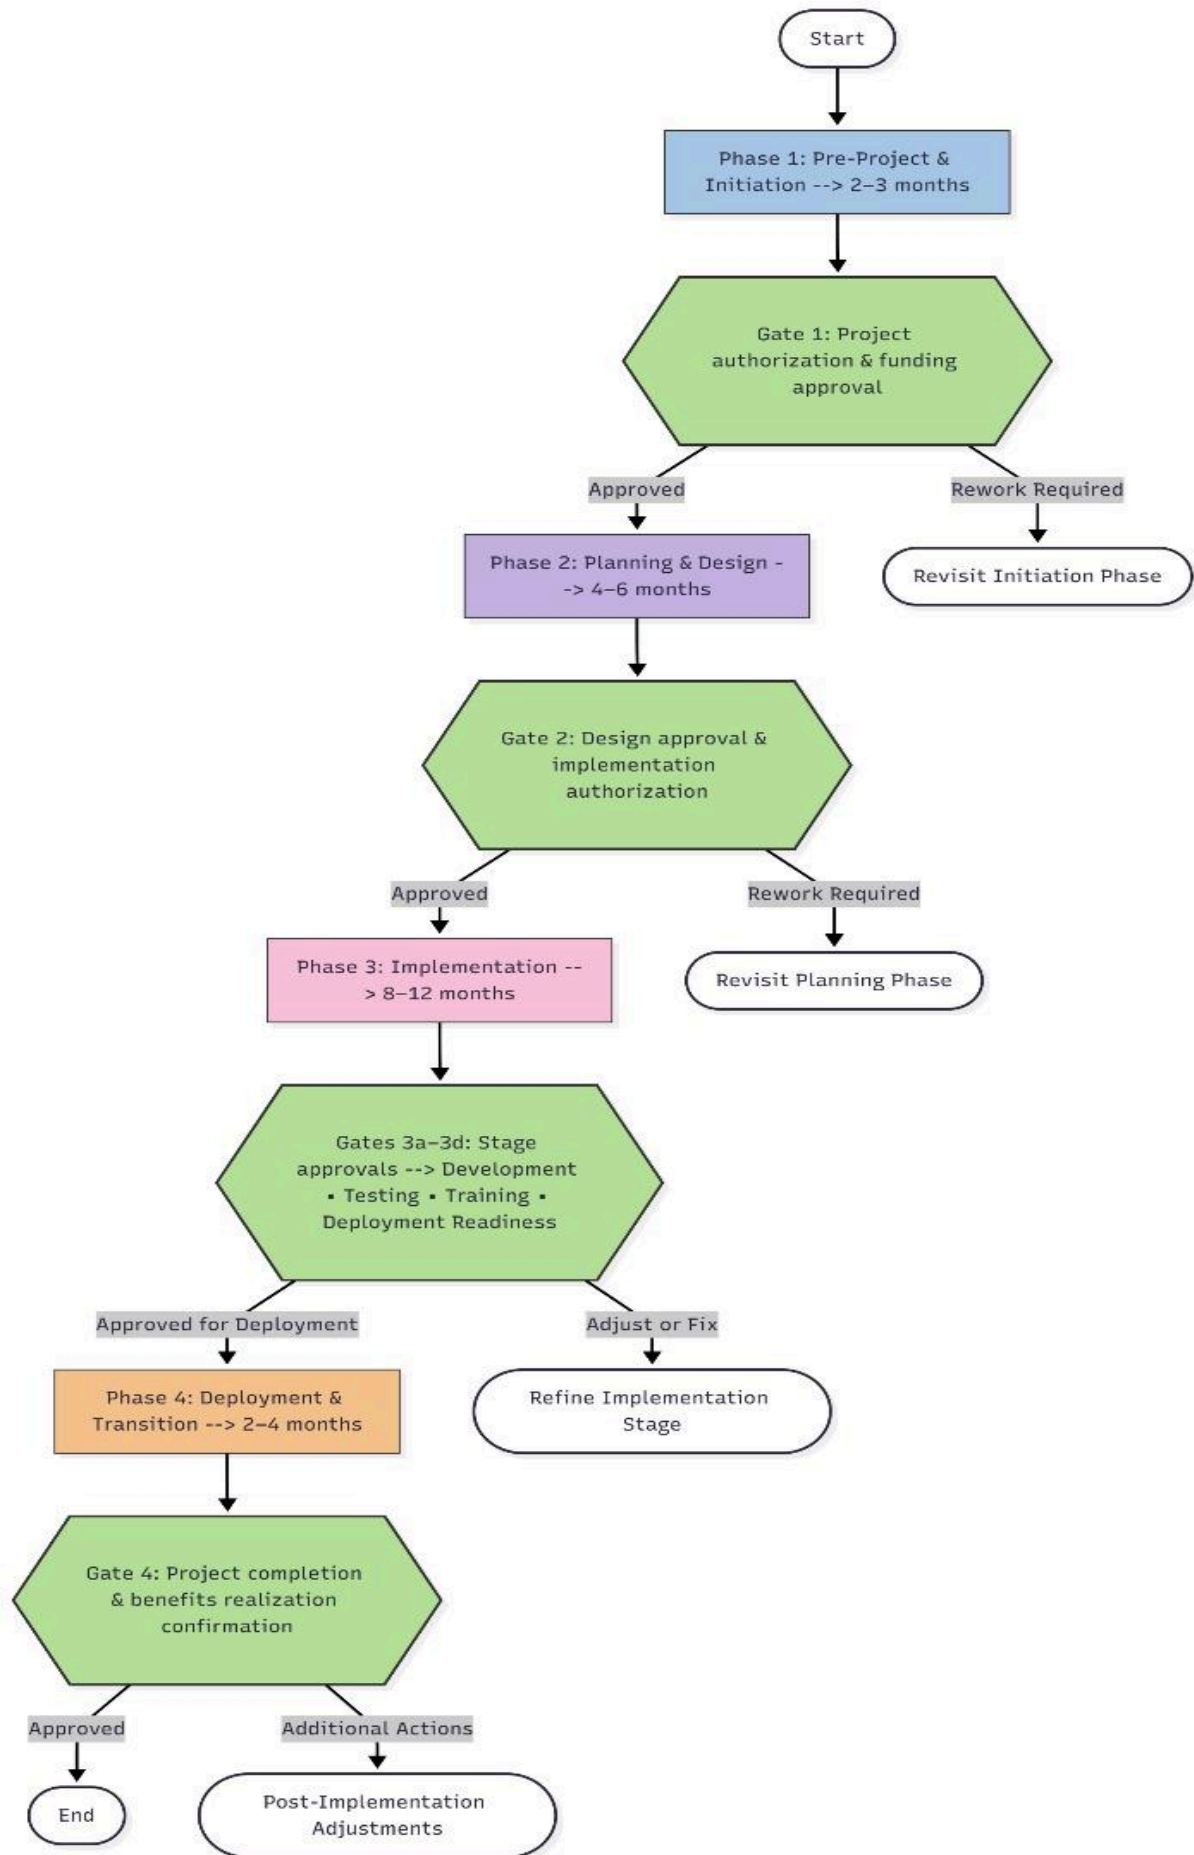

## **Project 2 : Infrastructure Upgrade Project**

### **Phase 1: Project Initiation (1 month)**

#### **Key Activities:**

- Infrastructure assessment and baseline establishment
- Stakeholder identification and requirements confirmation
- Project charter development
- Initial risk assessment
- Team mobilization
- Procurement planning

#### **Deliverables:**

- Infrastructure Assessment Report
- Project Charter
- Stakeholder Register
- Requirements Specification
- Risk Register
- Procurement Strategy

#### **Decision Gate:**

Gate 1: Project authorization and team confirmation

### **Phase 2: Detailed Planning & Design (2 months)**

#### **Key Activities:**

- Detailed work breakdown structure creation
- Technical design and specifications
- Resource scheduling and allocation
- Quality assurance planning
- Safety and compliance planning
- Vendor selection and contracting

#### **Deliverables:**

- Work Breakdown Structure
- Master Schedule
- Technical Design Documents
- Resource Management Plan
- Quality Assurance Plan
- Safety Plan
- Vendor Contracts

### **Decision Gate:**

Gate 2: Design approval and procurement authorization

## **Phase 3: Procurement & Preparation (2 months)**

### **Key Activities:**

- Equipment procurement and delivery
- Site preparation activities
- Testing environment setup
- Installation planning
- Team training and certification
- Change management preparation

### **Deliverables:**

- Procured Equipment and Materials
- Prepared Installation Sites
- Test Environment
- Installation Procedures
- Trained Team Members
- Change Management Plan

### **Decision Gate:**

Gate 3: Installation readiness confirmation

## **Phase 4: Implementation & Testing (5 months)**

### **Key Activities:**

- Infrastructure installation
- System configuration
- Integration testing
- Performance testing
- Security testing
- User acceptance testing
- Documentation completion

**Deliverables:**

- Installed Infrastructure
- Configured Systems
- Test Results and Reports
- Performance Validation
- Security Certificates
- User Acceptance Sign-off
- Technical Documentation

**Decision Gates:**

Gates 4a-4c: Installation completion, testing approval, and go-live authorization

**Phase 5: Deployment & Closure (2 months)**

**Key Activities:**

- Production cutover
- Operational support setup
- Performance monitoring
- Issue resolution and optimization
- Knowledge transfer
- Project closure and handover

**Deliverables:**

- Operational Infrastructure
- Support Procedures
- Performance Reports

- Optimization Recommendations
- Knowledge Transfer Documentation
- Project Closure Report
- Lessons Learned

#### **Decision Gate:**

Gate 5: Project completion and operational handover

### **Justification and references to standards:**

#### **PMBOK 7 References**

- Performance Domains: Planning (detailed upfront planning), Project Work (sequential execution), Delivery (predictable outcomes), Measurement (progress tracking)
- Development Approach: Predictive approach suitable for well-defined scope and requirements
- Tailoring: Traditional project management with formal documentation and stage gates

#### **PRINCE2 References**

- Themes: Business Case (infrastructure benefits), Plans (detailed planning), Quality (technical quality), Risk (technical and operational risks), Change (controlled changes), Progress (milestone tracking)
- Processes: Traditional stage-based approach with clear boundaries and deliverables
- Products: Emphasis on technical deliverables and documentation

#### **ISO 21500 References**

- Process Groups: Sequential implementation with clear phase boundaries
- Knowledge Areas: Scope (fixed requirements), Schedule (sequential activities), Cost (budget control), Quality (technical standards), Risk (infrastructure risks), Procurement (vendor management)
- Governance: Technical governance with operational oversight

### **Workflow Diagram**



